



VISVESVARAYA TECHNOLOGICAL UNIVERSITY

(State University of Government of Karnataka Established as per the VTU Act,1994)

"Jnana Sangama", Belagavi-590018 Karnataka State, India

2

7.1.4 Water conservation facilities available in the Institution:

2. Bore Well / Open well recharge provided at VTU, Jnana Sangama Belagavi

The bore wells that were defunct and having less yield were replenished and recharging of the bore wells were done by constructing recharge pits around the bore well. Such practices have resulted in improvement of groundwater table in the campus area. Maintenance of the system which includes cleaning of filter drains and recharge pits is carried out on regular basis by the engineering section.

Director

**Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018**



7.1.4 Water conservation facilities available in the Institution:



3

Director

Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018



7.1.4 Water conservation facilities available in the Institution:

Recharge Pit for Bore well




3
Director

**Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University
Belgavi - 590018**



7.1.4 Water conservation facilities available in the Institution:

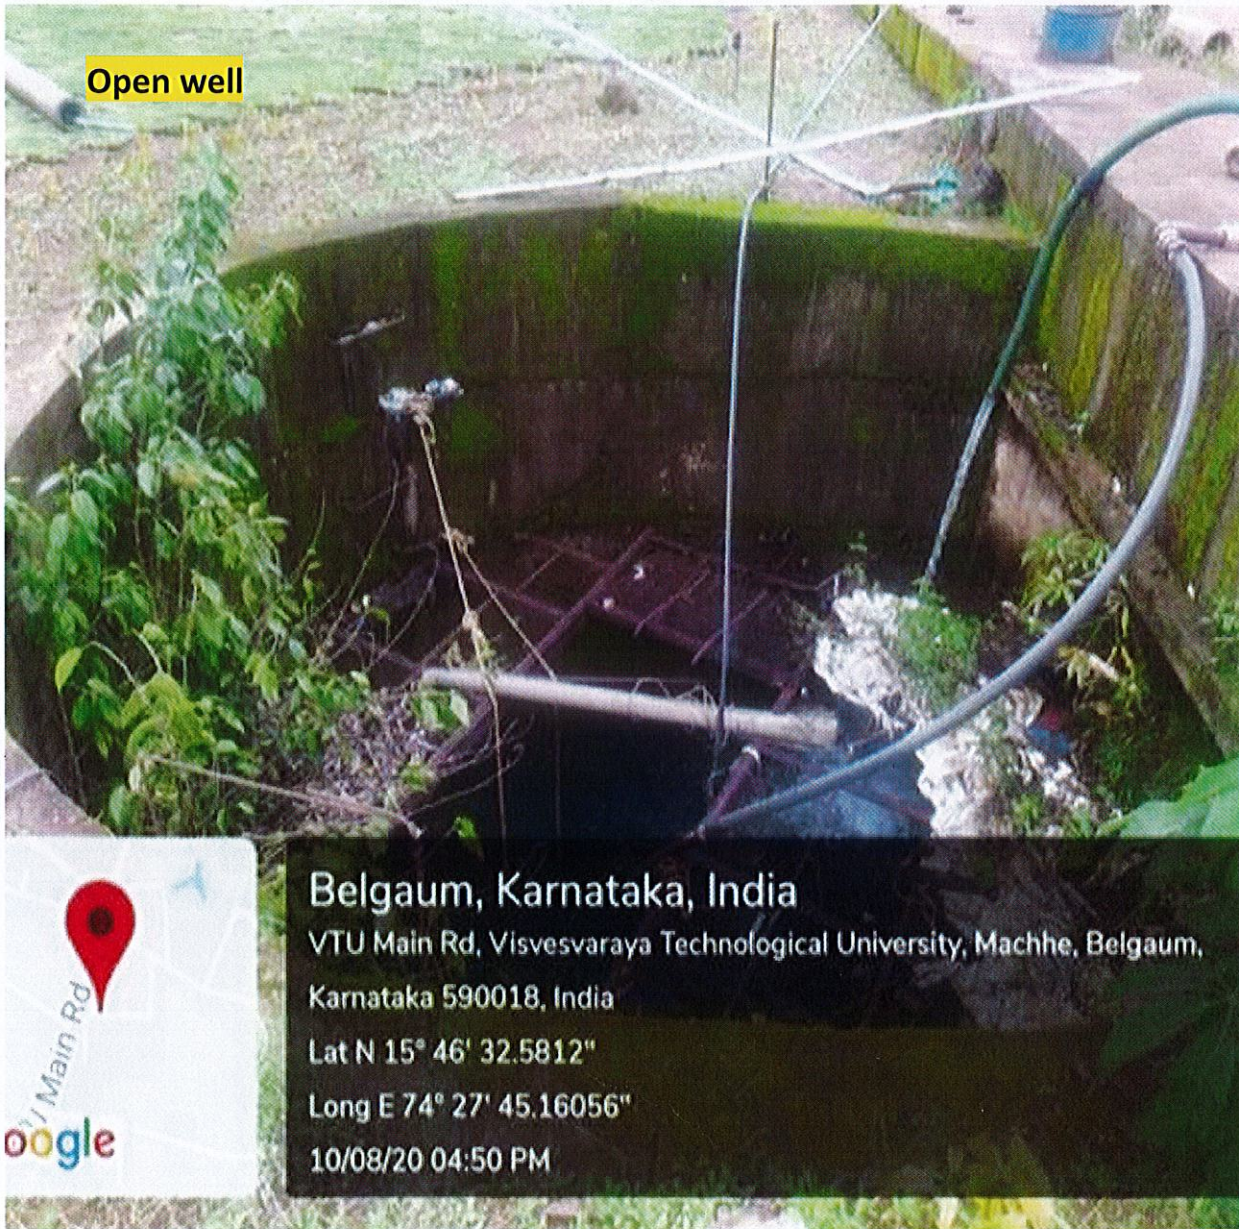

Director

Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

VISVESVARAYA TECHNOLOGICAL UNIVERSITY, BELGAUM

Name of work: Construction of Footpath & side drainage including percolation pits(for rain harvesting) along the ring road at VTU, "Jnana Sangama", Belgaum

Contractor: Sri B. G. Godse, Contractor, Belgaum

Agreement No.VTU/IRC No.27/2010-11, dated:30.8.2010

R.A. Bill No.3 & Final

Sl.No.	Description	Unit	Tender Qty	Rate	Previously Paid		Now to be paid		Upto Date	
					Qty	Amount	Qty	Amount	Qty	Amount
CIVIL WORKS										
WORK BELOW PLINTH										
1	Earthwork in surface excavation in ordinary soil for levelling and lowering the ground manually (other than foundation of buildings, culverts, road drains and trenches of pipe lines and cables) and removing the excavated stuff to all distance, excavated surface levelled and neatly dressed, disposed earth to be levelled and neatly dressed, disposed earth to be levelled after breaking of clods and neatly dressed as per specifications.	Cum	448.00	70.00	554.46	38812.2	0.00	0.00	554.46	38812.20
2	Providing and laying Stone dust for pathway including spreading watering tamping etc,. Complete as per specifications and direction of EIC.	Cum	396.00	175.00	355.26	62170.5	0.00	0.00	355.26	62170.50

Director

**Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018**

3	Providing and laying in position plain cement concrete of mix 1:3:6 using 40mm and down size graded granite metal machine mixed, concrete laid in layers not exceeding 15cms.thick well compacted, in foundation and plinth, including cost of all materials, labour, HOM of machinery, curing complete as per specificatios.	Cum	198.00	3090.00	240.01	741630.9	0.00	0.00	240.01	741630.90
4	Providing and fixing at site precast cement concrete M15 grade kerb, 425 cms wide and 10cms thick using 20mm and down granite metal including cost of materials, labour, curing complete as per specifications.	Rmt	2200.00	160.00	2375.4	380064	0.00	0.00	2375.40	380064.00
5	Providing and laying in position plain cement concrete of nominal mix 1:2:4 using 20mm and down size graded trap/basalt/granite metal machine mixed, concrete laid in layers not exceeding 15cms thick well compacted in foundation, plinth and cills , including cost of all materials labour, HOM of machinery, curing complete as per specifications.	Cum	760.00	4200.00	758.28	3184776	0.00	0.00	758.28	3184776.00
6	Providing and removing centring,shuttering strutting etc., and removal of form work for foundations, footings, bases of columns for mass concrete including cost of all materials, labour complete as per specifications.	Sqm	3520.00	120.00	3675.85	441102	0.00	0.00	3675.85	441102.00
7	Providing and laying heavy duty cobble stones 60mm thick intelock shape and colour with a minimum compressive strength of 281 kg per sqcm over 50mm thick cement mortar (average thickness) and compacting with plate virator having 3tons compaction force thereby forcing part of sand underneath to come up in between joints, final compaction of paver surface joints into its final level, including cost of materials, labour and HOM of machineries complete as per specifications.	Sqm	2200.00	450.00	2747.72	1236474	0.00	0.00	2747.72	1236474.00

Director

Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

8	Providing and laying reinforced cement concrete pipe 150mm dia NP2 for culverts including pointing ends, and fixing collars with cement mortar 1:2 including cost of all materials, labour, curing complete as per specifications.	Rmt	400.00	260.00	228	59280	0.00	0.00	228.00	59280.00
9	Providing and laying reinforced cement concrete pipe NP3 for culverts including pointing ends, and fixing collars with cement mortar 1:2 including cost of all materials, labour, curing complete as per specifications.	Rmt	83.00	2000.00	83.9	167800	0.00	0.00	83.90	167800.00

PART-'B'										
1	Earhtwork excavation of 1.20 to 1.50 M. External diameter to a depth up to 3 M. Well through all types of strata namely Sandy soil, Ordinary soil, hard soil, and soft rock without blasting complete as per drawing and technical specification. Depth of sinking is recorded from bed level complete .rates including setting out compaction of shoring and braking,dresing of sides and bottom and backfilling with aprovel materials.	Cum	160.00	200.00	0	0	143.15	28630.00	143.15	28630.00
2	Providing and laying reinforced cement concrete Rings of 1.20 to 1.50 Mt. dia and 350 to400 mm depth for well sticing with suitable weep holes including cost of material, labour,curing complete as per specifications.	Nos	240.00	900.00	0	0	200.00	180000.00	200.00	180000.00
3	Providing weep holes in Brick masonry / Plain / Reinforced concrete abutment, wing wall / return wall with 100mm dia AC pipe extending through the full width of the structure with slope of 1V : 20 H towards drawing foce. Complete as per drawing and technical specificatins complete as per spcifications.	Nos	180.00	150.00	0	0		0.00	0.00	0.00

Director

**Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018**

4	Providing and laying of Filter media with granular materials / stone crushed aggregates satisfying the requirements laid down in clause 250004.2.2 of MORTH specification to a thickness of not less than 300mm.	Cum	65.00	700.00	0	0	74.57	52199.00	74.57	52199.00
5	Providing 10cm thick RCC 1:1.5: 3 concrete for perforated drawing of 1500mm dia with suitable perforated holes as per drawings using clean granite or trap jelly of 20mm and down size with necessary reinforcement at 20cm.C/C both the ways of 8mm dia including formwork centing, curing, finishing the exposed faces with CM 1:3 etc., complete.	Sqm	55.00	800.00	0	0	54.78	43824.00	54.78	43824.00
TOTAL RS.							6312109.60	304653.00		6616762.60
SAY RS.							6312109.00	304653.00		6616762.00

Assistant Executive Engineer,
VTU, Belgaum

Resident Engineer,
VTU, Belgaum

Director

Internal Quality Assurance Cell -
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

24

Head of Account: 5001-101-101

Estimate Sanctioned for Rs. 4,99,849=00

Form P.W.G. 33 (Revised)

RUNNING ACCOUNTS BILL

(See Para 215)

2.5

(DUPLICATE)

Recharge Pit

(Final payment must be made on forms printed on yellow paper which should not be used for Intermediate payments)

For contractor: - This form provides for (1) Advance payments and (2) payments for measured works. The form of Account of secured Advances which has been printed separately should be attached where necessary.

Sub - Division

Division VISVESVARAYA TECHNOLOGICAL UNIVERSITY, BELGAUM dated _____

Cash Book Vr. No. --
Sri Suresh C. Hooli, Belagavi

Name of Contractor _____

Name of Work Providing of Recharge pit & Hydrofacturing for existing Bore wells in VTU Campus, Jnana Sangama, Belagavi.

Serial No. of this bill R.A. Bill No.1st & Final

No. and date of his/her previous bill for this work _____

Reference to Agreement No VTU/IRC-05/2020-21, Dt:06-07-2020

Date of written order to commence work 07-07-2020

Due Date of completion of work 20-08-2020

Actual Date of Completion: 18-08-2020

I. ACCOUNT OF WORK EXECUTED

Item of work (Grounded under 'Sub Heads' and Sub-works of estimate)	Unit	Rate	Quantity executed up to date as per Measurement Book	Payment on the basis of actual measurements up to date/since Previous bill		Remarks
				5	6	
1	2	3	4	5	6	7
SEPARATE SHEETS ARE ENCLOSED						

Director

Total value of work done to date (A) :Rs. 4,57,726.00

Deduct Value of work shown on previous Bill :Rs. 0.00

Net Value work since previous Bill (P) :Rs. 4,57,726.00

Figures (F) in words Rupees Rs. Four Lakhs Fifty Seven Thousand Seven Hundred Twenty Six only

Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

When there are two or more entries in column 6 relating to cash Sub-Head of estimate they should in the case of works the accounts of which are kept by Sub-Heads, be totaled and the total recorded in column for posting the works abstract

(P.T.O.)

II. CERTIFICATES AND SIGNATURE

To Measurements on which are based the entries in columns 1 to 6 of Account I were made by **Sri Jayappa, Asst. Engr., VTU, Belagavi**

On 20-08-2020

and re-recorded at page

Measurements recorded in M.B. No.2238, page from 13 to 17

2. Certified that in addition to and quite apart from the quantities of work actually executed at shown in column 4 of Account I, some work has actually been done in connection with several items, and value of such work (after deducting there from the proportionate amount of secured advance, if any ultimately recoverable on account of the quantities or materials used therein) is in no case, less than the advance payment as per items 2 of the memorandum of payment made as proposed to be made for the convenience of the contractor, in anticipation of and subject to the results of the details measurements, which will be made as soon as possible & measurements checked by **Resident Engineer, VTU, Belgaum.**

Dated Signature of Officer

(Signature)
20/8/2020
Preparing the bill

(Rank)

(Rank)

(Signature)

Signature of Contractor

Dated Signature of the Officer Authorising
Resident Engineer
VTU, Belagavi
Payment

(All measurements are accepted full & final)

This Certificate must be signed by the Sub-Divisional or Divisional Officer.

This Signature is necessary only when the Officer who prepares the bill is not the Officer who authorise the payment in such case the two signature are essential.

III MEMORANDUM OF PAYMENTS

Rs. 4,57,726.00

- Total value of work actually measured as per Account I, Column 5 Entry (A)
- Total 'up-to-date' advance payment for work not yet measured as per details given below:

Rs.	P. (-)	(B)
-----	--------	-----

(a) Total as per previous bill	(-)	(b) Since previous bill
--------------------------------	-----	-------------------------

as per page of M.B. No.

- Total 'Up-to-date' Secured advance of Security or materials as per Annexure (from 26A) Column 3 Entry (c).

- Total (Items 1 +2 +3)

- Deduct amount with held (a) From previous bill as per last running Account bill
Figures for Works abstract

Rs.	P.	(b) From this bill.
-----	----	---------------------

- Balance i.e. 'Up-to-date' payments (items 4-5) (K)

- Total amount of payment already made as per entry (K) of last Running Account Bill No. Rs. 0.00
of forwarded with Accounts for 19

Rs. 4,57,726.00

(Signature)
Director

**Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018**

VISVESVARAYA TECHNOLOGICAL UNIVERSITY, BELGAUM

NAME OF WORK : Providing of Recharge pit & Hydrofacturing for existing Bore wells in VTU Campus, Jnana Sangama, Belagavi.

Estimated Amount : Rs 4,99,849.00

Tendered Amount : Rs 4,59,999.00

Agency : Sri S.C. Hooli

Ageement Number : VTU/IRC No.05/2020-21, dated:06-07-2020

Date of Work Order : VTU/BGM/RE/ AE/2020-21/1102/1 Date 06-07-2020

Date Of Commencement : 07-07-2020

Due Date of Completion : 20-08-2020

Actual Date of Completion 18-08-2020

Date of Recording 20-08-2020

RA BILL-1st and Final

I No	Item	Unit	Tender Qty	Tender Rate	Previously Paid		Now to be paid		Upto Date	
					Qty	Amount	Qty	Amount	Qty	Amount
1	Earthwork excavation by manual means for foundation of buildings, culverts,water spply and sanitary lines and electrical conduits etc, eithe in pits or in trenches 1.5 m and above in width, in hard soil not exceeding 1.5 m. In depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from the edges of excavation with lead up to 50 m. including breaking of clods complete as per specifications. ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Cum	131.18	200.0	0.00	0.00	130.90	26180.00	130.90	26180.00

247


Director

**Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018**

2.7

I No	Item	Unit	Tender Qty	Tender Rate	Previously Paid		Now to be paid		Upto Date	
					Qty	Amount	Qty	Amount	Qty	Amount
2	Providing and laying in position plain cement concrete of mix 1:3:6 with OPC cement @ 220kgs, with 40mm and down size graded granite metal coarse aggregates @0.892cum and fine aggregates @ 0.465cum machine mixed, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation including cost of all materials, labour, HOM of machinery, curing complete as per specifications. ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Cum	6.23	3000.0	0.00	0.00	6.19	18570.00	6.19	18570.00

246



Director
Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

2.8

I No	Item	Unit	Tender Qty	Tender Rate	Previously Paid		Now to be paid		Upto Date	
					Qty	Amount	Qty	Amount	Qty	Amount
3	Providing and laying in position reinforced cement concrete of design mix M20 with OPC cement @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @ 0.46cum, with superplasticiser @3lts conforming to IS9103-1999 Reaffirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in ground floor level for roof slabs, staircase, lintles, and beams retaining walls, return walls, walls (any thickness) including attached plasters, columns, pillars, posts, struts, buttresses, string or lacing courses, parapets, coping, bed blocks, anchor blocks, plain window cills, fillets etc., including cost of all materials, labour, HOM of machinery, curing, complete but excluding cost of reinforcement as per specifications. ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Cum	5.36	5000.0	0.00	0.00	5.34	26700.00	5.34	26700.00

245

3

Director
Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

2.9

I No	Item	Unit	Tender Qty	Tender Rate	Previously Paid		Now to be paid		Upto Date	
					Qty	Amount	Qty	Amount	Qty	Amount
4	Providing and constructing granite / trap / basalt size stone masonry in foundation with cement mortar 1:6, stone hammerd dressed in courses not less than 20 cms high, bond stones at two m. apart in each course including cost of materials, labour, curing complete as per specifications. ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Cum	10.37	2000.0	0.00	0.00	10.15	20300.00	10.15	20300.00
5	Providing and constructing granite / trap / basalt size stone masonry in basement with cement mortar 1:6, edges of stones chistle dressed in courses not less than 15 cms high, bond stones at two m. apart in each course including cost of materials, labour, curing complete as per specifications. ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Cum	11.18	2000.0	0.00	0.00	10.93	21860.00	10.93	21860.00
6	Providing ruled pointing to coursed stone masonry with cement mortar 1:3, 20mm deep, after raking joints to depth of 20mm nicely lining, including cost of materials, labour, curing complete as per specifications -- - The Bidders Should qualify all the Conditions mentioned in the bid document	Sqm	49.68	146.0	0.00	0.00	48.60	7095.60	48.60	7095.60

huz



Director
Internal Quality Assurance Cell
 Page 4 (IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

2-10

I No	Item	Unit	Tender Qty	Tender Rate	Previously Paid		Now to be paid		Upto Date	
					Qty	Amount	Qty	Amount	Qty	Amount
7	Providing and laying Pitching on slopes laid over prepared filter media including boulder apron laid dry in front of toe of embankment complete as per drawing and Technical specifications A. Stone / Boulder MORTH Specification No. 2504 ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Cum	90	500.0	0.00	0.00	88.20	44100.00	88.20	44100.00
8	Supply of coarse sand ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Cum	7.2	4000.0	0.00	0.00	7.20	28800.00	7.20	28800.00
9	Supplying and spreading Charcoal ---- The Bidders Should qualify all the Conditions mentioned in the bid document	Kg	400	500.0	0.00	0.00	400.00	200000.00	400.00	200000.00
10	Drilling holes of size 3.50mm to 4.0mm dia. To casing pipe upto 1 m. depth ---- The Bidders Should qualify all the Conditions mentioned in the bid document	No	300	100.0	0.00	0.00	300.00	30000.00	300.00	30000.00
11	Providing aqua nylon mesh for sand filter ---- The Bidders Should qualify all the Conditions mentioned in the bid document	LS	4	1000.0	0.00	0.00	4.00	4000.00	4.00	4000.00
12	Supplying and Binding with Nylon Rope ---- The Bidders Should qualify all the Conditions mentioned in the bid document	LS	4	30.0	0.00	0.00	4.00	120.00	4.00	120.00

243

Director

Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

2.11

I No	Item	Unit	Tender Qty	Tender Rate	Previously Paid		Now to be paid		Upto Date	
					Qty	Amount	Qty	Amount	Qty	Amount
13	Hydrofracking of 150mm to 165mm dia. Bore wells by using Hydrofracturing unit using single packer with minimum of two fractures including transportation unit supporting vehicle, crew charges, cost of all consumables and yield testing of bore wells one hour at once before fracturing and the other after fracturing within a radius of 50km. from taluka head quarters including supplying necessary water for fracturing etc; complete ---- The Bidders Should qualify all the Conditions mentioned in the bid document	each	3	5000.0	0.00	0.00	3.00	15000.00	3.00	15000.00
14	Cleaning of bore well including yield testing of bore well either using slow or fast rig for not more than two hours at the final depth with a minimum working of two hours continuously with air compressor or suitable pump as per specification including the cost of transportation charges , crew charges, cost of all consumables etc; complete ---- The Bidders Should qualify all the Conditions mentioned in the bid document	each	3	5000.0	0.00	0.00	3.00	15000.00	3.00	15000.00
Total Amount Rs						0.00		457725.60		457725.60
Say Rs						0.00		4,57,726.00		4,57,726.00

24/2

[Signature]

CONTRACTOR

[Signature]

Director

Internal Quality Assurance Cell (IQAC)

Visvesvaraya Technological University, Belgavi - 590018

[Signature]
2/2/21
Assistant Engineer
VTU, Belagavi

[Signature]
Resident Engineer
VTU, Belagavi

2/2



ವಿಶ್ವೇಶ್ವರಯ್ಯ ತಾಂತ್ರಿಕ ವಿಶ್ವವಿದ್ಯಾಲಯ, ಬೆಳಗಾವಿ 2-13

Visvesvaraya Technological University
"Jnana Sangama" Belagavi -590 018, Karnataka State

Prof. A. S. Deshpande B.E., M.Tech., Ph.D..
REGISTRAR

Phone : (0831) 2498100
Fax : (0831) 2405467

Ref. No. VTU/BGM/RE/AE/2020-21/ 1102/1

Date: 06 JUL 2021

Issue of Notice to proceed with the work

To,

Sri S. C. Hooli,
"Prabhu Krupa,
74/40, Hanuman Nagar,
T.V. Center,
Belagavi

Sir,

Sub: Providing of Recharge Pit & Hydrofacturing for existing bore-wells in VTU Campus, "Jnana Sangama", Belagavi - Reg..

Ref: 1. This office letter of acceptance No. VTU/BGM/RE/AE/2019-20/9963, dated: 02.03.2020.

2. Performance Security Deposit in the form of Bank Guarantee No.SCH 3/20, dated: 13.03.2020 for Rs.23,000/- of KVGB., Belagavi(Valid Upto 13.03.2021)

3. Un-balanced Performance Security Deposit in the form of Bank Guarantee No.SCH 4/20, dated:04.07.2020 for Rs.40,000/- of KVGB., Belagavi(Valid Upto 13.10.2020)

Pursuant to your furnishing the requisite Security Deposit and signing of the contract agreement for the work of *Providing of Recharge Pit & Hydrofacturing for existing bore-wells in VTU Campus, "Jnana Sangama", Belagavi* for the Contract Price of Rs.4,59,999=00 (*Rupees Four Lakhs Fifty Nine Thousand Nine Hundred Ninety Nine only*) i.e.,7.9724% below the estimated amount. You are hereby instructed to proceed with the execution of the said services in accordance with the specification and tender conditions of the contract documents.

Yours faithfully,

Sd/-
REGISTRAR,
VTU.,Belagavi

Copy to:

- 1)The Hon'ble V.C., VTU, Belagavi through Secretary to V.C., VTU Belagavi for information.
- 2)The Finance Officer, VTU, Belagavi for information.
- 3)The Resident Engineer, VTU, Belagavi for necessary action.
- 4)File.

Director

**Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018**

REGISTRAR,
VTU.,Belagavi

2.15

Whereas the Employer is desirous that the contractor execute the work of *Providing of Recharge Pit & Hydrofacturing for existing bore-wells in VTU Campus, "Jnana Sangama", Belagavi* vide tender Notification No.VTU/ BGM/RE/2019-20/IFT No.30/5784, dated: 11-10-2019 (hereinafter called "the Works) and the Employer has accepted the Tender by the Contractor for the execution and completion of such Works and the remedying of any defects therein at a contract price of *Rs.4,59,999=00 (Rupees Four Lakhs Fifty Nine Thousand Nine Hundred Ninety Nine only) i.e.,7.9724% below the estimated amount of Rs.4,99,849.00*, for tender period of 45 (Forty Five) Days.

NOW THIS AGREEMENT WITNESSTH as follows:

1. In this Agreement, words and expression shall have the same meanings as are respectively assigned to them in the Conditions of Contract hereinafter referred to, and they shall be deemed to form and be read and construed as part of this Agreement.
2. In consideration of the payments to be made by the Employer to the Contractor as hereinafter mentioned, the Contractor hereby covenants with the Employer to execute and complete the Works and remedy any defects therein in conformity in all aspects with the provisions of the Contract.
3. The Employer hereby covenants to pay the Contractor in consideration of the execution and completion of the Works and the remedying the defects wherein the Contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.
4. The following documents shall be deemed to form and be read and construed as part of this Agreement, viz:
 - i) Letter of Acceptance;
 - ii) Notice to proceed with works;
 - iii) Contractor's Tender;
 - iv) Contract Data;
 - v) Conditions of contract (including Special Conditions of Contract
 - vi) Specifications;
 - vii) Drawings;
 - viii) Bill of Quantities; and
 - ix) Any other document listed in the Contract Data as forming part of the contract.

In witness whereof the parties there to have caused this Agreement to be executed the day and tear first before written.


The common Seal of _____ was hereunto affixed in the presence of:

Signed, Sealed and Delivered by the said The Registrar, Visvesvaraya Technological University, "Jnana Sangama", Belagavi - 590 018

In the presence of: The Resident Engineer, Visvesvaraya Technological University, "Jnana Sangama", Belagavi - 590 018


CONTRACTOR


Director
Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018

REGISTRAR, VTU, BELAGAVI


2.16

VISVESVARAYA TECHNOLOGICAL UNIVERSITY

Completion Certificate

- 1) Name of work: Providing of Recharge pit & Hydrofacturing for existing Bore wells in VTU Campus, Jnana Sangama, Belagavi.
- 2) Name of contractor: Sri Suresh C. Hooli, Belagavi
- 3) Date of commencement: 07-07-2020
- 4) Actual Due date of completion: 20-08-2020
- 5) Actual date of completion: 18-08-2020
- 6) Estimated cost: Rs. 4,99,849.00
- 7) Cost put to tender: Rs. 4,99,849.00
- 8) Cost of work at tendered rate: Rs. 4,59,999.00
- 9) Actual expenditure incurred: Rs.4,57,726.00
- 10) Whether the work has been completed satisfactorily: "Yes"

CERTIFICATE

Certified that the work has been completed satisfactorily as per the terms and conditions of contract agreement and as per prescribed specifications.

REGISTRAR,
VTU, BELAGAVI


Director
Internal Quality Assurance Cell
(IQAC)
Visvesvaraya Technological University,
Belgavi - 590018
